



DEPARTMENT OF PURCHASING & CONTRACT COMPLIANCE

**Winner 2000- 2006 Achievement of Excellence in Procurement Award
National Purchasing Institute**

Jerome Noble, Director



November 28, 2007


**Re: 07ITB58334A-CJC
Supply and installation of Uninterruptible Power Supply System**

Dear Bidders:

Attached is one (2) copy of Addendum 2, hereby made a part of the above referenced 07ITB58334A-CJC, Supply and Installation of Uninterruptible Power Supply System

Except as provided herein, all terms and conditions in the **ITB** referenced above remain unchanged and in full force and effect.

Sincerely,


Charlie Crockett
Assistant Purchasing Agent

07ITB58334A-CJC
Supply and installation of Uninterruptible Power Supply System

Addendum No. 2
Page Two

This Addendum forms a part of the contract documents and modifies the original ITB documents as noted below:

➤ Below are Questions and Answers submitted for the aforementioned bid.

Question #1

Will the county provide us with the structural floor loading information for the existing raised floor? The computer room floors will generally support a 300 PSF load and a concentrated load of 1000 PSF or the industry standard existing in 1996, whichever is lower.

Question #2

Ramp into room is damaged and probably in need of repair. Will the county repair this floor prior to commencing this contract? If not, is it to be included in the scope of this contract? Ramp will be repaired before work begins on the UPS replacement.

Question #3

Will the county provide us with the data center floor plan showing existing equipment racks and any proposed or planned equipment racks as prior to bid date? No.

Question #4

Is the ultimate goal of the county to have 2 ups systems strictly for redundancy (N+1) and a final build out capacity of 225 KVA? Or is it the county's goal to have dual UPS for a capacity system with an ultimate build out of 450 KVA? The ultimate capacity would be 450 kVA

Question #5

Who is responsible for electrical permitting? There is no need for permitting

Question #6

Is the county going to provide professional engineer stamped drawings for this project or is it to be the scope of the awarded contractor? This will be in the scope of contract. County does not require PE stamped drawings

07ITB58334A-CJC


Supply and installation of Uninterruptible Power Supply System

Addendum No. 2

Page Three

Question #7

Is any of the open space on the data center floor available for the setting of the first 225 KVA UPS module and battery? If not, what are the restricted areas?

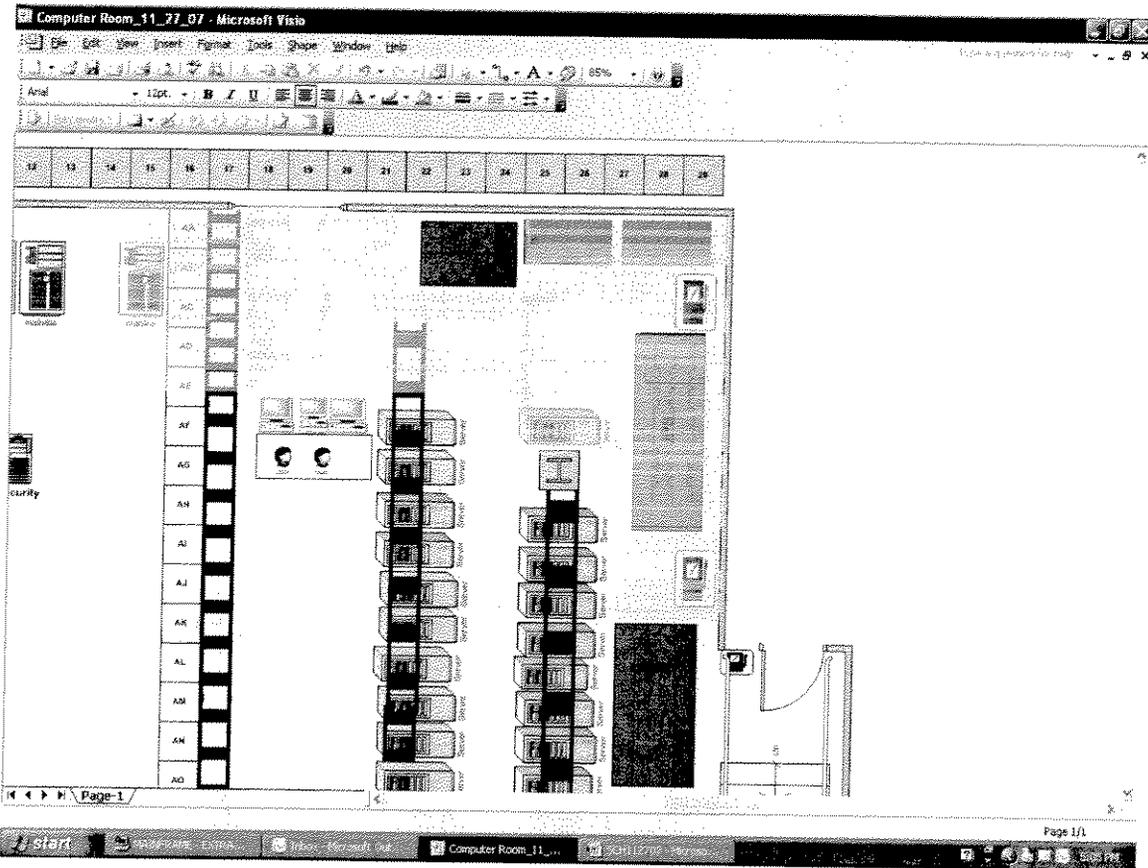

Question #8

Is it the intention of the county to have 2 separate switchboards feed each UPS system? One switchboard will feed both UPS systems

Question #9

Is it the intention of the county to have the mechanical systems upgraded if necessary to support the new UPS equipment? No

Question #10

If the equipment manufacturer's recommend cooling which differs from the existing capability, does the county want this as an optional adder to the base bid? Or should the value for mechanical build-out be included in the base bid? The value for mechanical build-out shall be included in the base bid?

07ITB58334A-CJC

Supply and installation of Uninterruptible Power Supply System

Addendum No. 2

Page Four

Question #11

How many years of system preventative maintenance do you want included in the base bid? Do you want options for annual extensions to service contracts? (1) Initially for two years after expiry of warranty. (2) Yes

Question # 12

What is the size of the load being supported – Average load around 125 kVA

Question #13

What is the equipment being supported – Information Technology Data Center

Question #14

What is the amount of runtime they are looking for in the event of a power outage – 30 minutes

Question #15

Do they have a generator - Yes

Question #16

What do they have for input power – 480 Volts, 3 phases AC

Question #17

What do they need for output power – Can't be in one sentence. Vendor needs to refer the spec.

Question #18

How large is the room that they are installing these UPS's – 7000 Sq. Ft

Question #19

Does it have removable ceiling tiles or raised floors – Removable ceiling tiles and raised floor

Question #20

Do they need remote management – No, need remote monitoring

Question #21

Do they need a rack mounted solution – Not against rack mounted solution.

Question #22

Is there air conditioning in the room? What is their current set up like – Three Liebert units support the air-conditioning in the area

07ITB58334A-CJC
Supply and installation of Uninterruptible Power Supply System

Addendum No. 2
Page five

ACKNOWLEDGEMENT OF ADDENDUM NO.2

The undersigned proposer acknowledges receipt of this addendum by returning one (1) copy of this form with the proposal package to the Purchasing Department, Fulton County Public Safety Building, 130 Peachtree Street, Suite 1168, Atlanta, Georgia 30303 by the ITB due date and time **December 6, 2007 at 11:00 A.M.**

This is to acknowledge receipt of Addendum No.2, _____ day of _____, 2007.

Legal Name of Bidder

Signature of Authorized Representative

Title
